



NORTH CAROLINA
Department of Transportation

2024-2033 STIP Development

May 2022

Today's Topics


- Background
- STIP Development
- STIP Format
- Project Prioritization Status
- Next Steps / Schedule
- Discussion



Background

STIP Budget Changes

COVID – Revenues affected



\$8B+ in cost increases since July 2020 (1,000+ estimates updated)

- Many increases due to outdated or low estimates
- Processes in place to ensure more accurate estimates moving forward

New budgets provided \$3.8B in additional revenue

- Federal Infrastructure Investment and Jobs Act (IIJA)/Bipartisan Infrastructure Law (BIL)
- State Budget

Inflation adjustments

- Board of Transportation approved changing from 1% compounded annually to 3% (\$2.5B impact)

2024-2033 STIP Funding Availability for Committed Projects

Statewide Mobility

Available Funding	Programming Status
\$10.6B	\$3.36B Over

Regional Impact

Region	Available Funding	Programming Status
A (D1 & D4)	\$647.5M	\$383.2M Over
B (D2 & D3)	\$919.2M	\$391.2M Over
C (D5 & D6)	\$1.78B	\$297.1M Over
D (D7 & D9)	\$1.33B	\$596.7M Over
E (D8 & D10)	\$1.67B	\$756.5M Over
F (D11 & D12)	\$881.0M	\$455.7M Over
G (D13 & D14)	\$676.1M	\$982.2M Over

REG Total: \$3.86B Over

Division Needs

Division	Available Funding	Programming Status
1	\$569.7M	\$129.5M Over
2	\$569.7M	\$190.3M Over
3	\$569.7M	\$77.3M Under
4	\$569.7M	\$223.2M Under
5	\$569.7M	\$172.4M Over
6	\$569.7M	\$87.4M Under
7	\$569.7M	\$65.4M Under
8	\$569.7M	\$85.3M Over
9	\$569.7M	\$31.6M Under
10	\$569.7M	\$68.8M Over
11	\$569.7M	\$102.4M Under
12	\$569.7M	\$234.0M Over
13	\$569.7M	\$325.7M Over
14	\$569.7M	\$88.2M Over

DIV Total: \$706.9M Over

Total Overprogrammed: \$8B

Includes estimated funding from Infrastructure and Investment Jobs Act (IIJA)/Bipartisan Infrastructure Law (BIL)

As of January 25, 2022. Available Funding reflects accounting for 3% inflation. Programming Status Amounts are compared to 100% of budget.

2024-2033 STIP Development

Prioritization Workgroup Overall Goals

Develop trustworthy and dependable STIP (fiscally constrained)

Produce 2024-2033 STIP using current STIP project list with transparent process

Have an opportunity to fund new projects in P7 scoring (all 22 STI funding categories)

Ensure process is grounded in state/federal requirements

2024-2033 STIP Development (Framework)

Only includes projects funded in 2020-2029 STIP

Projects selected for funding using one of two approaches:

1. Delivery Projects – programmed first
 - Currently scheduled for CON in FY 2024, 2025, or 2026; ROW underway; or has federal grant
2. P3-P4-P5 Evaluation (Seniority Approach) – programmed second

Opportunity to swap projects & project schedules following release of Draft STIP (April 25th)

- Swaps must be agreed to by NCDOT and MPO/RPO(s)
- Cost of project(s) swapped in must be within 10% of cost of project(s) being swapped out

2024-2033 STIP Development (General Observations)

Delivery Projects:

- Schedules for >80% of projects did NOT change!



P3-P4-P5 Evaluation (Seniority Approach):

- Schedules for 34% of projects did NOT change
- # and length of schedule changes varies by STI category


Other:

- Some non-committed projects were programmed to meet STI minimum funding requirements


2024-2033 STIP Development (Project Specific)

[Insert project specific items here]


2024-2033 STIP Development – Visual

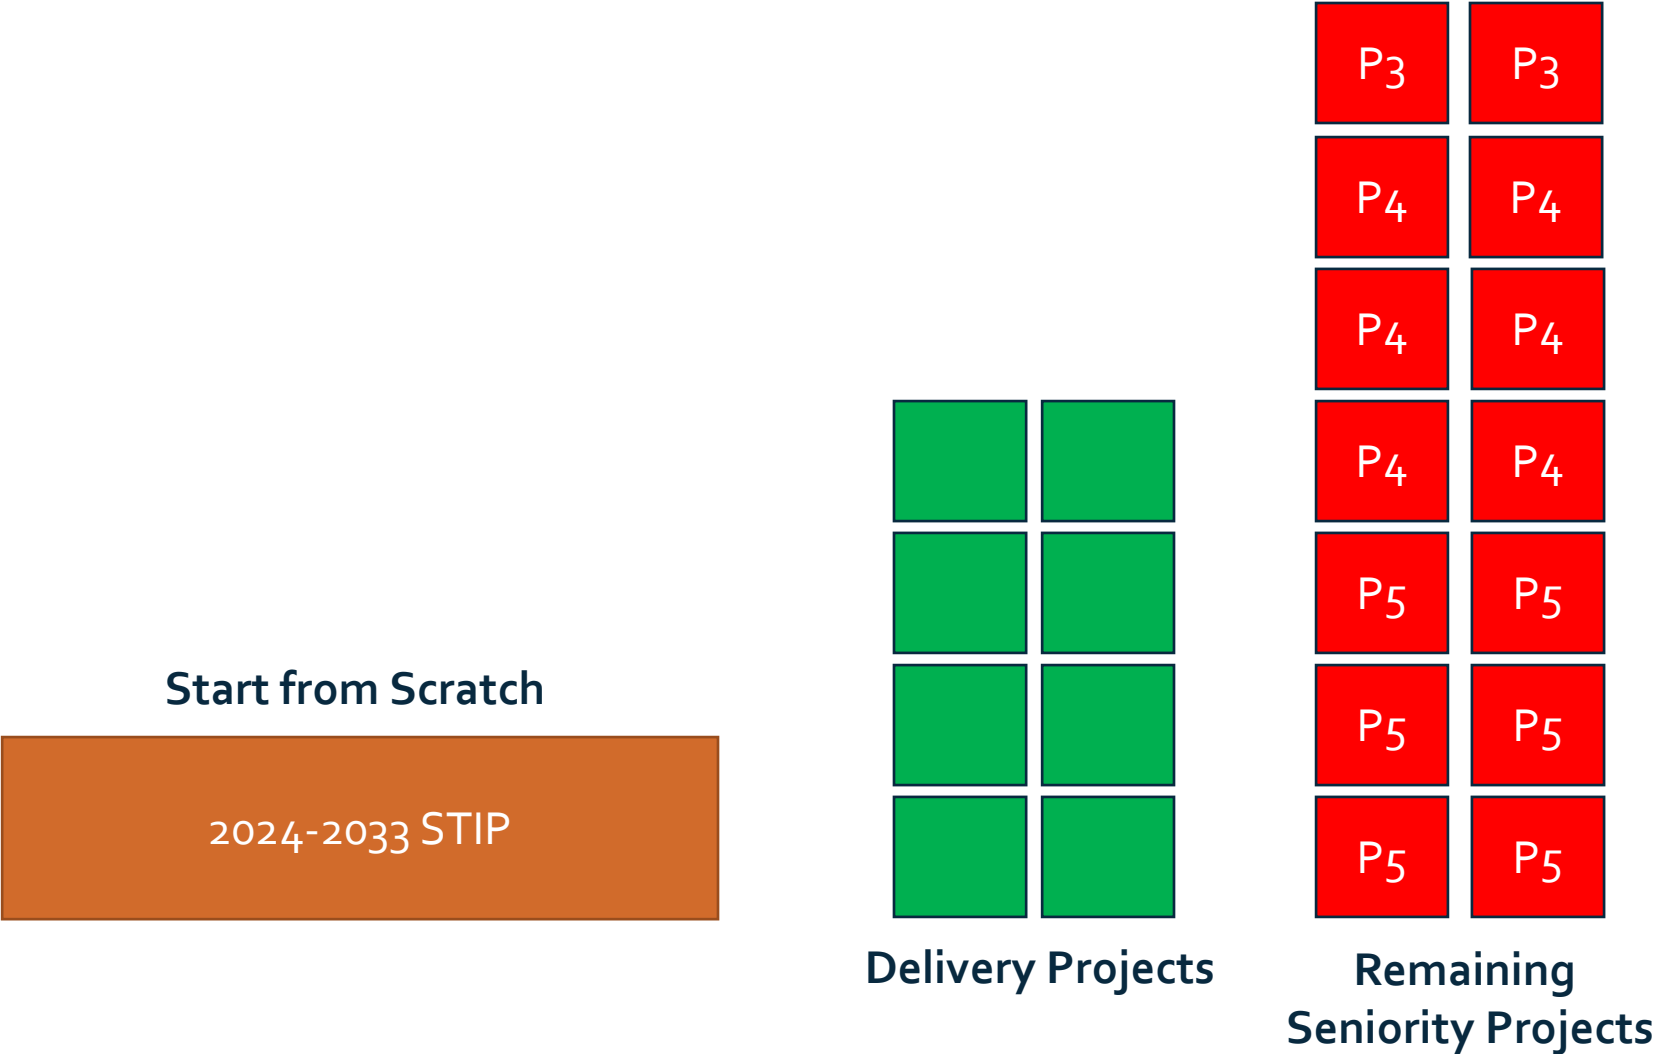


2024-2033 STIP Development – Visual

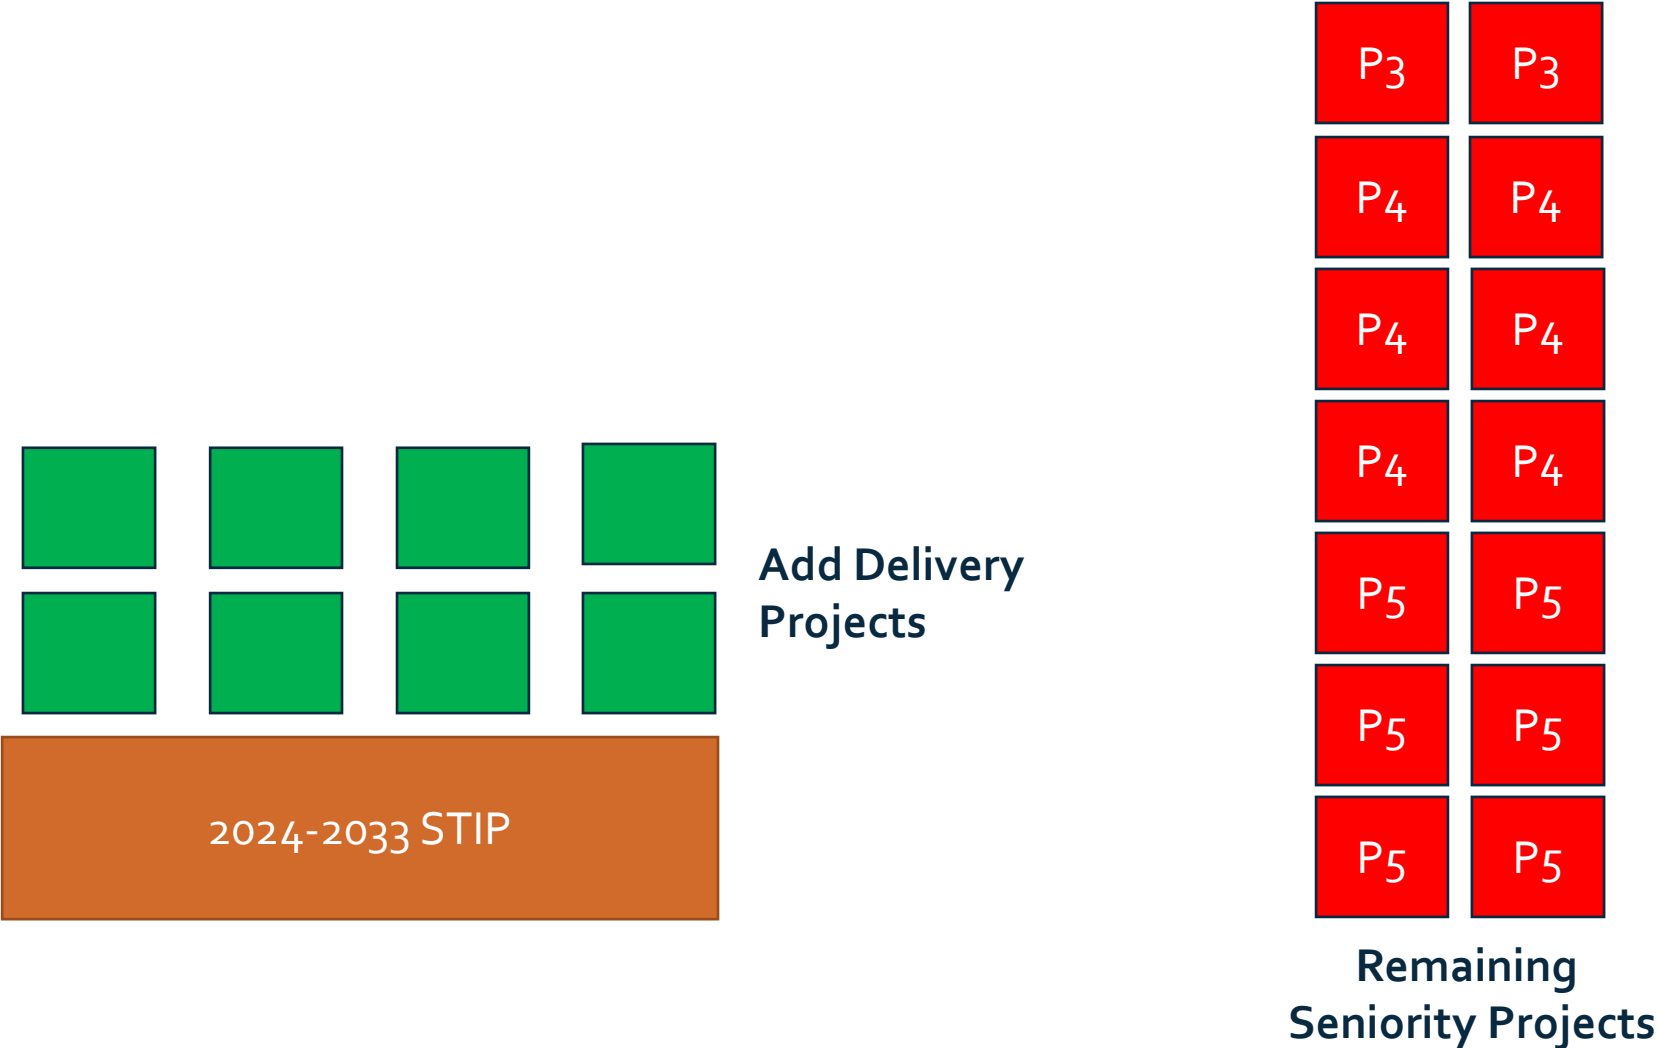

2024-2033 STIP Development – Visual

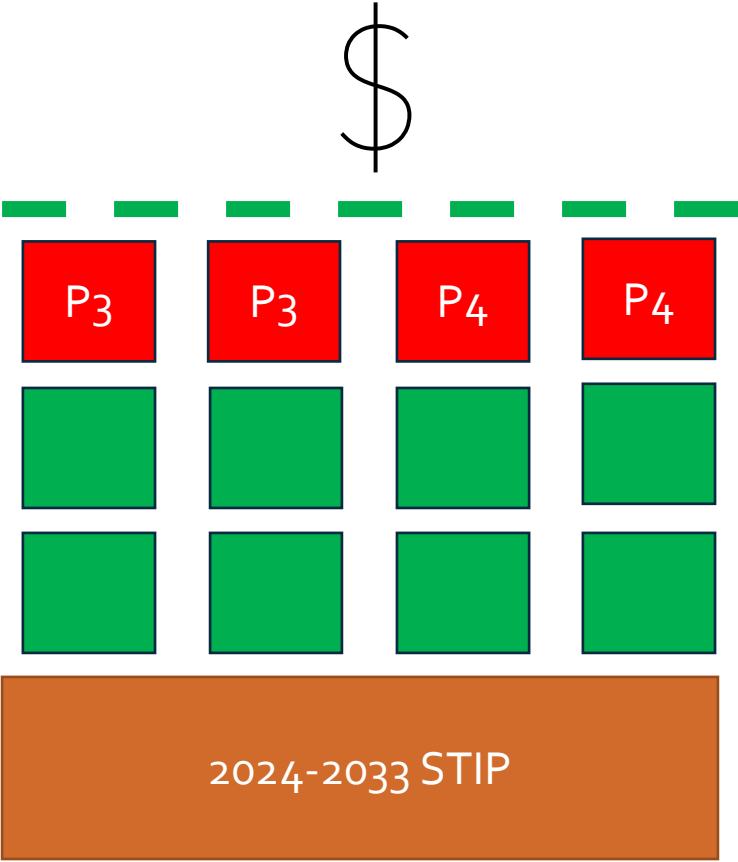


Add additional projects following seniority approach until budget is expended for each funding bucket





Remaining Seniority Projects

2024-2033 STIP Development – Visual

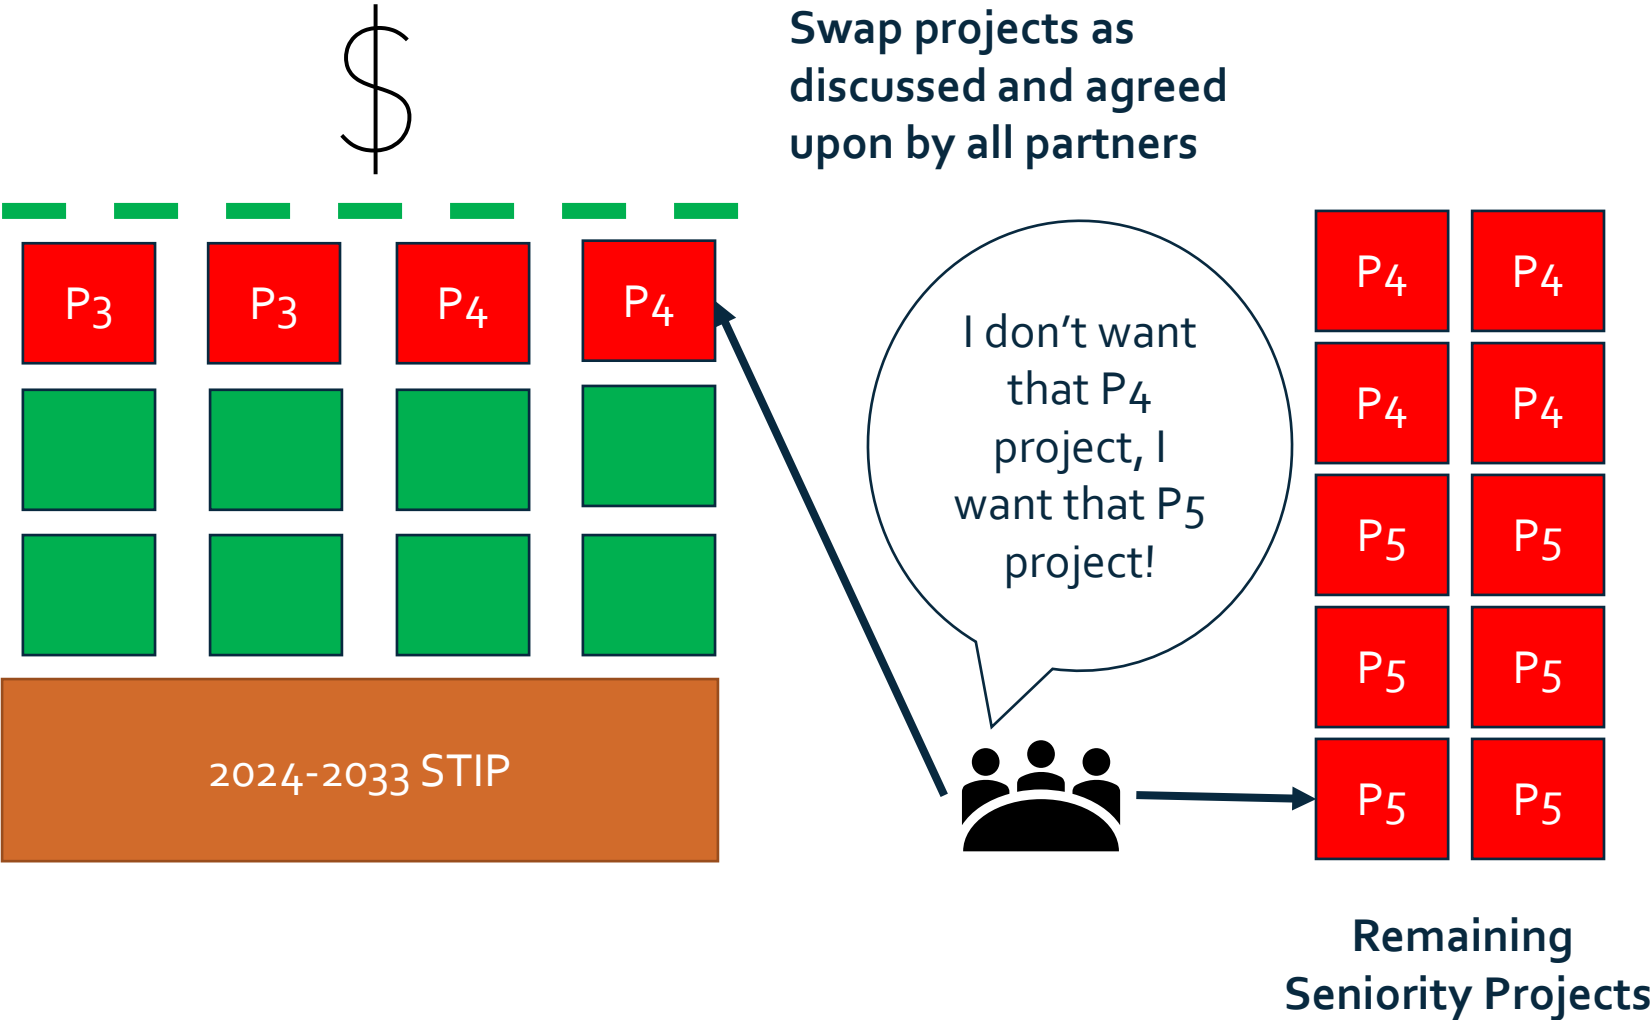


2024-2033 STIP Development – Visual

Release Revised Draft STIP

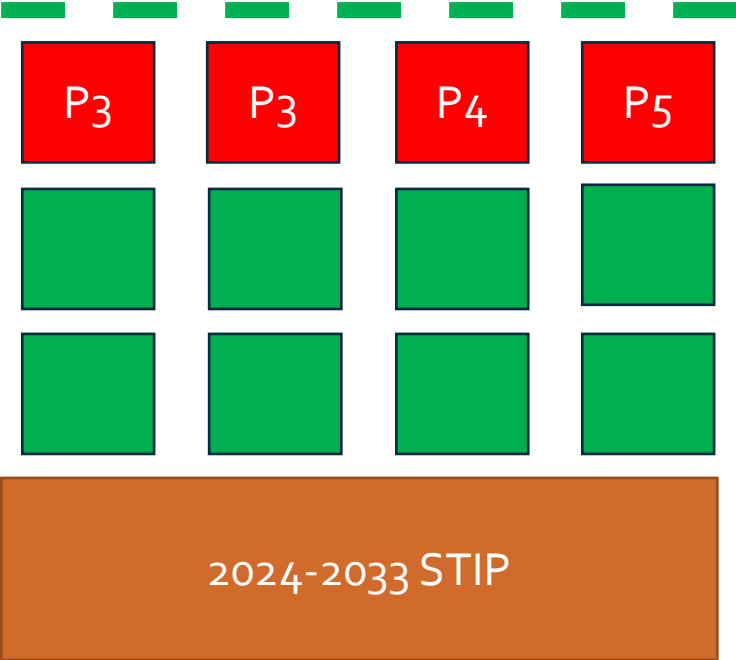

Much better!

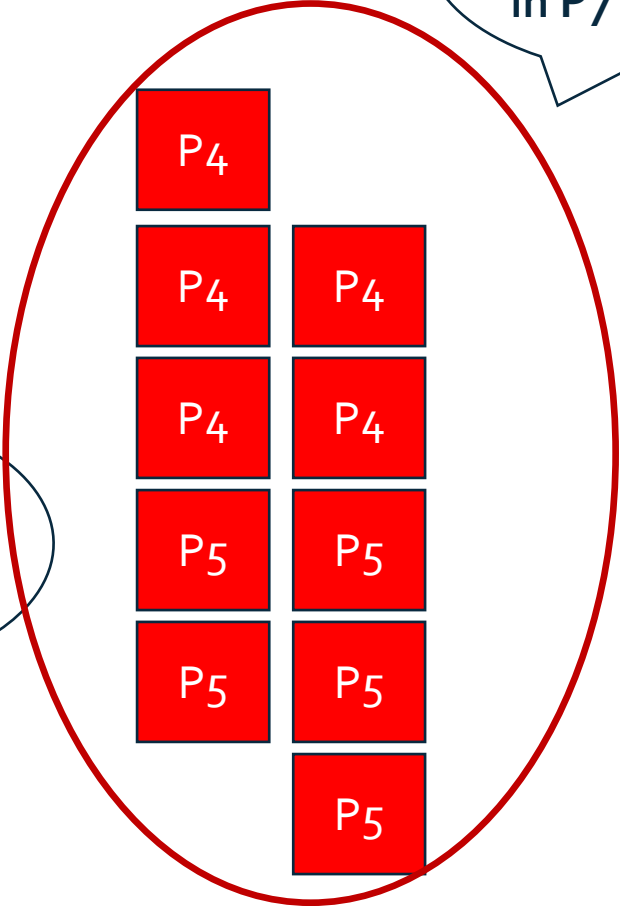

Projects reprioritized in P7 scoring


Remaining Seniority Projects

A Sample Swap for DERPO

Swap R-5727 Morehead City Bridges Street Extension (\$76.7m) for:

- R-5884 Emerald Isle Loon St Roundabout (\$2m)
- R-5886 Emerald Isle Coast Guard St. Roundabout (\$3.6m)
- R-5962 Beaufort Live Oak/Cedar St. Roundabout (\$5.4m) or R-5946 Beaufort Live Oak/Lennoxville Rd. intersection upgrades (\$7.8m)
- P-5742 Newport NCR/US 70 grade separation (\$14.4m)
- R-5945 Beaufort US 70 (NC 101 to Olga Rd.) access management (\$56m)

Total cost for swapped projects: (\$81.4m/83.8m, both under 110% of R-5727 cost.)



2024-2033 STIP Format

2024-2033 STIP Format – Excel-based



2024-2033 DRAFT STATE TRANSPORTATION IMPROVEMENT PROGRAM

NOTES: PROJECT DATA SHOWN ARE FOR FORMAT DEMONSTRATION PURPOSES ONLY. THESE RECORDS AND DATA DO NOT REPRESENT ACTUAL PROJECTS.

BASIC PROJECT INFORMATION							PRIORITIZATION INFORMATION					FISCAL YEAR PROJECT PHASE SCHEDULED TO START						COMMENT
COUNTY(S)	ROUTE	DESCRIPTION	MODE	DIVISION(S)	MPOs/RPOs	PROJECT ID	STI CATEGORY FUNDED	CURRENT PRIORITIZATION STATUS	ELIGIBLE FOR SWAP	FUNDING SOURCE (SEE FUNDING SOURCES TAB FOR MORE INFO)	RIGHT-OF-WAY PROJECTED SCHEDULE	STI FUNDS NEEDED FOR RIGHT-OF-WAY	UTILITIES PROJECTED SCHEDULE	STI FUNDS NEEDED FOR UTILITIES	CONSTRUCTION PROJECTED SCHEDULE	STI FUNDS NEEDED FOR CONSTRUCTION	TOTAL STI FUNDS	
ALAMANCE	BURLINGTON-ALAMANCE REGIONAL AIRPORT (BUY)	RUNWAY EXTENSION.	AVIATION	7	BURLINGTON-GRAHAM MPO	AV-8446	DIVISION 7	SCHEDULED FOR DELIVERY	YES	L, T	2024	\$1,200,000					\$1,200,000	
ALAMANCE	US 31 (COLUMBUS ROAD)	SR 5158 (MEMPHIS ROAD) / OLIVE LANE INTERSECTION. INSTALL TRAFFIC SIGNAL AND ADD TURN LANES.	HIGHWAY	7	BURLINGTON-GRAHAM MPO	U-7489	REGION D	SCHEDULED FOR DELIVERY	YES	T	2025	\$600,000	2025	\$400,000	2027	\$1,100,000	\$2,100,000	
BUNCOMBE	I-70	SR 6234 (2ND AVENUE) - EXIT 276. CONSTRUCT INTERCHANGE IMPROVEMENTS.	HIGHWAY	13	FRENCH BROAD RIVER MPO	I-6246	REGION G	WILL BE REPRIORITIZED	YES	NHP	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$2,660,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$500,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$5,200,000	\$8,360,000	
BUNCOMBE	I-70	NC 25 (HIGH CLIFF BOULEVARD) - EXIT 278 TO SR 6532 (HOLCOMBE AVENUE). CONSTRUCT AUXILIARY LANES.	HIGHWAY	13	FRENCH BROAD RIVER MPO	I-6912	DIVISION 13	SCHEDULED FOR DELIVERY	YES	NHP	2023	\$2,500,000	2023	\$1,100,000	2025	\$9,600,000	\$13,200,000	
BUNCOMBE	SR 6452 (BRUGHS MILL ROAD)	US 219 TO NC 815 (CRIPPLE CREEK ROAD). WIDEN TO MULTI-LANES.	HIGHWAY	13	FRENCH BROAD RIVER MPO	U-6498	DIVISION 13	SCHEDULED FOR DELIVERY	YES	BGANY	2027	\$43,200,000	2027	\$5,600,000	2029	\$23,600,000	\$72,400,000	
CABARRUS	VARIOUS	WRIGHT ROAD, DEPOT ST TO SHADY PINE LANE. CONSTRUCT SIDEWALK AND BIKE LANES.	HIGHWAY	10	CABARRUS-ROWAN MPO	EB-9845	DIVISION 10	SCHEDULED FOR DELIVERY	YES	CMAQ, L, BGANY	2023	\$1,200,000			2024	\$2,650,000	\$3,850,000	
CABARRUS	US 127	REPLACE BRIDGE 120987 AND BRIDGE 120985 OVER DICKENS BRANCH.	HIGHWAY	10	CABARRUS-ROWAN MPO	B-8012	REGION E	SCHEDULED FOR DELIVERY	NO	NHPB	2023	\$750,000	2023	\$625,000	2024	\$9,800,000	\$11,175,000	
CLEVELAND, RUTHERFORD	US 33 FULLERTON BYPASS	EAST OF NC 234 TO EAST OF NC 25. GRADING, STRUCTURES, AND PAVING.	HIGHWAY	12, 13	GASTON-CLEVELAND-LINCOLN MPO, Foothills RPO	R-6727C	REGION F	SCHEDULED FOR DELIVERY	NO	T					2020	\$51,420,000	\$51,420,000	BUILD NC BOND FUNDING: \$1.336M FOR CONSTRUCTION PAYBACK 2021-2035 (FY 2021-2035); \$11.336M FOR CONSTRUCTION PAYBACK FY 2020-2034 (FY 2020-2034); \$28.609M FOR CONSTRUCTION PAYBACK 2021-2035 (FY 2021-2035).
CUMBERLAND	SR 6504 (WILLIS CREEK ROAD)	PLEASANT HILL ROAD TO SR 7878 (CRUMPLER RD). UPGRADE ROADWAY.	HIGHWAY	6	FAYETTEVILLE AREA MPO	U-6807	DIVISION 6	SCHEDULED FOR DELIVERY	YES	T	2028	\$8,652,000	2028	\$8,080,000	2030	\$12,600,000	\$29,332,000	
DURHAM	I-70	PORTER ROAD TO WEST OF NC 59. PAVEMENT REHABILITATION.	HIGHWAY	5	DURHAM-CHAPEL HILL-CARRBORO MPO	I-6933	STATEWIDE MOBILITY	SCHEDULED FOR DELIVERY	NO	NHPIM					2026	\$12,167,000	\$12,167,000	
DURHAM	I-70	US 79. INTERCHANGE IMPROVEMENTS.	HIGHWAY	5	DURHAM-CHAPEL HILL-CARRBORO MPO	U-7465B	STATEWIDE MOBILITY	WILL BE REPRIORITIZED	YES	NHP	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$91,472,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$638,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$81,302,000	\$173,412,000	
DURHAM	US 79	NC 265 TO RIDGEMONT AVENUE. CONSTRUCT OPERATIONAL IMPROVEMENTS.	HIGHWAY	5	DURHAM-CHAPEL HILL-CARRBORO MPO	U-6118	REGION C	WILL BE REPRIORITIZED	YES	T	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$450,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$250,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$2,325,000	\$3,025,000	
HERTFORD	NC 10	NORTHAMPTON COUNTY LINE TO MEHERRIN RIVER.	HIGHWAY	1	PEANUT BELT RPO	R-7256A	DIVISION 1	SCHEDULED FOR DELIVERY	NO	T	2023	\$350,000	2023	\$7,850,000	2023	\$29,600,000	\$37,800,000	
HERTFORD	NC 10	MEHERRIN RIVER TO US 258.	HIGHWAY	1	PEANUT BELT RPO	R-7256B	DIVISION 1	SCHEDULED FOR DELIVERY	YES	T	2023	\$7,025,000	2023	\$8,750,000	2025	\$18,500,000	\$34,275,000	

Note: These are not actual projects. Data shown is for illustrative purposes only.

2024-2033 STIP Format – Print on 11x17

Print



Print

Copies: 1

Printer



PD193125 on dot-trbpp10

Ready

[Printer Properties](#)

Settings



Print Active Sheets

Only print the active sheets

Pages:

to



Print One Sided

Only print on one side of...



Collated

1,2,3 1,2,3 1,2,3



Landscape Orientation



11x17

11" x 17"



Custom Margins



Fit All Columns on One Page

Shrink the printout so that it...

[Page Setup](#)

COUNTY		ROUTE	DESCRIPTION	DIVISION	MPO/RPO	PROJECT ID	STIP CATEGORY FUNDED	CURRENT PRIORITIZATION STATUS	ELIGIBLE FOR SWAP	FUNDING SOURCE (SEE FUNDING SOURCES TAB FOR MORE INFO)	RIGHT-OF-WAY BEGINS	STIP FUNDS NEEDED FOR RIGHT-OF-WAY	UTILITIES BEGINS	STIP FUNDS NEEDED FOR UTILITIES	CONSTRUCTION BEGINS	STIP FUNDS NEEDED FOR CONSTRUCTION	TOTAL STIP FUNDS	COMMENT
ALAMANCE	BURLINGTON-ALAMANCE REGIONAL AIRPORT (BURL)		RUNWAY EXTENSION.	7	BURLINGTON-GRAHAM MPO	AV-8446	DIVISION 7		YES	L T	2024	\$1,200,000					\$1,200,000	
ALAMANCE	US 31 (COLUMBUS ROAD)	SR 5158 (MEMPHIS ROAD) / OLIVE LANE INTERSECTION. INSTALL TRAFFIC SIGNAL AND ADD TURN LANES.	7	BURLINGTON-GRAHAM MPO	U-7489		REGION D		YES	T	2025	\$600,000	2025	\$400,000	2027	\$1,000,000	\$2,100,000	
BUNCOMBE	I-70	SR 6234 (2ND AVENUE) - EXIT 276. CONSTRUCT INTERCHANGE IMPROVEMENTS.	13	FRENCHBROAD RIVER MPO	I-6246		REGION G	WILL BE REPRIORITIZED	YES	NHP	FUNDED FOR PRELIMINARY	\$2,640,000	FUNDED FOR PRELIMINARY	\$500,000	FUNDED FOR PRELIMINARY	\$5,200,000	\$4,340,000	
BUNCOMBE	I-70	NC 25 (HIGH CLIFF BOULEVARD) - EXIT 278 TO SR 6522 (MOLCOMBE AVENUE). CONSTRUCT AUXILIARY LANES.	13	FRENCHBROAD RIVER MPO	I-6912		DIVISION 13		YES	NHP	2023	\$2,500,000	2023	\$1,100,000	2025	\$9,600,000	\$13,200,000	
BUNCOMBE	SR 6462 (BRUGH'S MILL ROAD)	US 219 TO NC 815 (DRIPPLE CREEK ROAD). WIDEN TO MULTILANES.	13	FRENCHBROAD RIVER MPO	U-6468		DIVISION 13		YES	BGANV	2027	\$43,200,000	2027	\$5,800,000	2029	\$23,600,000	\$72,400,000	
CABARRUS	VARIOUS	WRIGHT ROAD, SPOT ST TO SHADY PINE LANE. CONSTRUCT SIDEWALK AND BIKE LANES.	10	CABARRUS-ROMAN MPO	FB-5945		DIVISION 10		YES	CMAQ, L, BGANV	2023	\$1,200,000			2024	\$2,650,000	\$3,850,000	
CABARRUS	US 127	REPLACE BRIDGE 12097 AND BRIDGE 12098 OVER DICKENS BRANCH.	10	CABARRUS-ROMAN MPO	R-8012		REGION E		NO	NHP	2023	\$750,000	2023	\$625,000	2024	\$9,800,000	\$11,175,000	
CLEVELAND	US 33 FULLERTON BYPASS	EAST OF NC 234 TO EAST OF NC 25. GRADING, STRUCTURES, AND PAVING.	12, 13	GASTON-CLEVELAND-LINCOLN MPO, FOOT HILLS RPO	R-6727C		REGION F		NO	T					2020	\$59,420,000	\$5,142,000	BUILD NC BOND FUNDING: \$4,021 FOR PPE, PAYBACK 2021-2035 (FY 2021 / YR 26.3 SALE); \$11,336M FOR GDN, PAYBACK FY 2020-2034 (FY 2020 / YR 15 SALE); \$2,660M FOR GDN, PAYBACK 2023-2025 (YR 26.3 SALE).
CUMBERLAND	SR 6524 (WILLS CREEK ROAD)	PLEASANT HILL ROAD TO SR 3678 (CRUMPER ROAD). UPGRADE ROADWAY.	6	TARTRIVILLE AREA MPO	U-6807		DIVISION 6		YES	T	2028	\$8,652,000			2030	\$2,600,000	\$29,332,000	
DURHAM	I-70	POKER ROAD TO WEST OF NC 518. PAVEMENT REHABILITATION.	5	DUHAM-CHARL HILL-CARRBORO MPO	I-6953		STAT FWDR MOBILITY		NO	NHPIM					2026	\$12,167,000	\$12,167,000	
DURHAM	I-70	US 75. INTERCHANGE IMPROVEMENTS.	5	DUHAM-CHARL HILL-CARRBORO MPO	U-7465B		STAT FWDR MOBILITY	WILL BE REPRIORITIZED	YES	NHP	FUNDED FOR PRELIMINARY	\$9,142,000	FUNDED FOR PRELIMINARY	\$638,000	FUNDED FOR PRELIMINARY	\$85,202,000	\$17,412,000	
DURHAM	US 75	NC 285 TO RIDGEMONT AVENUE. CONSTRUCT OPERATIONAL IMPROVEMENTS.	5	DUHAM-CHARL HILL-CARRBORO MPO	U-6118		REGION C	WILL BE REPRIORITIZED	YES	T	FUNDED FOR PRELIMINARY	\$450,000	FUNDED FOR PRELIMINARY	\$250,000	FUNDED FOR PRELIMINARY	\$2,225,000	\$3,025,000	
HERTFORD	NC 10	NORTH HAMPTON COUNTY LINE TO MS HERRIN RIVER.	1	FRANKLIN RPO	R-2256A		DIVISION 1		NO	T	2023	\$7,850,000	2023	\$25,600,000	2023	\$25,600,000	\$37,800,000	
HERTFORD	NC 10	MEMPHIS RIVER TO US 208.	1	FRANKLIN RPO	R-2256B		DIVISION 1		YES	T	2023	\$7,025,000	2023	\$6,750,000	2025	\$58,500,000	\$64,275,000	
MADISON	US 51 (MALDEN BOULEVARD)	SR 7033 (KINGS DRIVE) TO NC 34 (STIRLING STREET). MODERNIZE ROADWAY.	13	LAND-OF-SKY RPO	R-8513		DIVISION 13	WILL BE REPRIORITIZED	YES	BGUS	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$4,100,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$2,700,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$24,100,000	\$30,900,000	
MIDWELL	US 51	SR 2654 (GARVEY AVENUE) TO SR 5511 (BRAINTREE ROAD).	13	FOOT HILLS RPO	R-2888A		NOT FUNDED	WILL BE REPRIORITIZED	NO	NHP	NOT FUNDED	\$8,200,000	NOT FUNDED	\$6,100,000	NOT FUNDED	\$95,450,000	\$133,100,000	
MOORE	NC 620	SR 4643 (NEWBRIDGE AVENUE) TO SR 5150 (HEDSAW LANE). CONSTRUCT OPERATIONAL IMPROVEMENTS.	8	TRIANGLE AREA RPO	U-9408		DIVISION 8		YES	T	2024	\$9,800,000	2024	\$980,000	2026	\$58,200,000	\$28,980,000	BUILD NC BOND: \$5 MILLION FOR RIGHT-OF-WAY - PAYBACK 2024-2038 (FY 2024 / YR 6 SALE)
NEW HANOVER	NC 130 (GARDEN GROVE PARKWAY)	STRATFORD ROAD TO NC 810 (SUNRISE AVENUE). MULTILANES ON NEW LOCATION.	3	WILMINGTON URBAN AREA MPO	U-6495		DIVISION 3		YES	BGANV	2027	\$49,976,000	2027	\$7,895,000	2029	\$89,225,000	\$147,096,000	
NEW HANOVER	SR 4745 (OLD PLANK ROAD)	SR 4736 (BAKERT CREEK ROAD) TO US 81 (FAIRVIEW AVENUE). WIDEN TO MULTILANES.	3	WILMINGTON URBAN AREA MPO	U-4540		DIVISION 3		YES	T	2028	\$8,300,000	2028	\$1,200,000	2030	\$58,336,000	\$27,836,000	
NEW HANOVER	US 81 (FAIRVIEW AVENUE)	NC 130 (GARDEN GROVE PARKWAY). UPGRADE INTERCHANGE.	3	WILMINGTON URBAN AREA MPO	U-8986		STAT FWDR MOBILITY		YES	T	2024	\$6,700,000	2024	\$1,500,000	2026	\$25,550,000	\$31,750,000	
NEW HANOVER	WILMINGTON	CONSTRUCT SIGNALIZED PEDESTRIAN CROSSING AT STRATFORD ROAD AND LAUREL AVENUE.	3	WILMINGTON URBAN AREA MPO	FB-6545		DIVISION 3		NO	L, TADA					2023	\$679,000	\$679,000	
ONSLOW	NC 136	NC 58 (OLD HILD ROAD) AND SR 4959 (BLUE LAKE DRIVE). UPGRADE PEDESTRIAN SIGNALS.	3	JACKSONVILLE URBAN AREA MPO	FB-2028A		STAT FWDR MOBILITY		NO	HSP					2022	\$45,000	\$45,000	
ONSLOW	NC 35 (WATSON AVENUE)	NC 53 (MOOPER ROAD) TO SR 8553. CONSTRUCT OPERATIONAL IMPROVEMENTS.	3	JACKSONVILLE URBAN AREA MPO	U-7531		REGION 8	WILL BE REPRIORITIZED	YES	T	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$14,500,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$7,980,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$38,080,000	\$61,460,000	
ONSLOW	NC 58	US 79 TO NC 58 (BROOKSIDE DRIVE). WIDEN TO MULTILANES.	3	JACKSONVILLE URBAN AREA MPO	U-7124		REGION 8	WILL BE REPRIORITIZED	YES	T	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$4,366,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$8,550,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$54,923,000	\$67,839,000	
ONSLOW	US 79	DEFERRING DRIVE TO MARGO AVENUE.	3	JACKSONVILLE URBAN AREA MPO	U-7375B		NOT FUNDED	WILL BE REPRIORITIZED	NO	NHP	NOT FUNDED	\$23,545,000	NOT FUNDED	\$1,180,000	NOT FUNDED	\$28,600,000	\$48,945,000	

Project Prioritization Status for the 2024-2033 STIP

Project Prioritization Status

BOT agreed to Workgroup Recommendation of a 5-year window

Projects with first year of ROW or CON in FY 2028 or earlier are “Scheduled for Delivery”

Projects with first year of ROW or CON in FY 2029 or later “Will be Reprioritized” in P7.0

Project Prioritization Status



2024-2033 DRAFT STATE TRANSPORTATION IMPROVEMENT PROGRAM: PROJECTS

NOTES: COSTS AND SCHEDULES ARE AS OF APRIL 25, 2022 AND ARE SUBJECT TO CHANGE. CURRENT PRIORITIZATION STATUS IS BASED ON THE PRIORITIZATION WORKGROUP'S RECOMMENDATION OF USING A FIVE-YEAR LIFECYCLE APPROACH. IF A PROJECT IS NOT SCHEDULED IN OR BEFORE FISCAL YEAR 2028, THE PROJECT IS CONSIDERED "SCHEDULED FOR DELIVERY" AND DOES NOT HAVE TO BE REPRIORITIZED). AT THIS TIME, THE BOARD OF TRANSPORTATION HAS APPROVED THE DRAFT STATE TRANSPORTATION IMPROVEMENT PROGRAM.

BASIC PROJECT INFORMATION							PRIORITIZATION INFORMATION			FISCAL YEAR PROJECT PHASE SCHEDULED TO START				
COUNTY(S)	ROUTE/CITY	DESCRIPTION	MODE	DIVISION(S)	MPOs/RPOs	PROJECT ID	STI CATEGORY FUNDED	CURRENT PRIORITIZATION STATUS	FUNDING SOURCE (SEE FUNDING SOURCES TAB FOR MORE INFO)	RIGHT-OF-WAY PROJECTED SCHEDULE	STI FUNDS NEEDED FOR RIGHT-OF-WAY	UTILITIES PROJECTED SCHEDULE	STI FUNDS NEEDED FOR UTILITIES	CONSTRUCTION PROJECTED SCHEDULE
ALAMANCE	BURLINGTON- ALAMANCE REGIONAL AIRPORT (BUY)	CONSTRUCT 100 FT PAVED OVERRUN AND MAKE SAFETY ENHANCEMENTS.	AVIATION	7	BURLINGTON-GRAHAM MPO	AV-5851	DIVISION 7	SCHEDULED FOR DELIVERY	T					2024
ALAMANCE	LEE AVENUE	WEST LEBANON AVENUE TO SR 1454 (WEST HAGGARD AVENUE) IN ELON. CONSTRUCT SIDEWALK.	BIKE/PED	7	BURLINGTON-GRAHAM MPO	EB-5988	DIVISION 7	SCHEDULED FOR DELIVERY	L, TA5200	2025	\$4,000			2026
ALAMANCE	I-40 / I-85	SR 1158 (HUFFMAN MILL ROAD) INTERCHANGE. CONSTRUCT ADDITIONAL LEFT TURN LANE ON I-40 WESTBOUND RAMP AND IMPROVE OPERATIONS AT SR 1308 (GARDEN ROAD) INTERSECTION.	HIGHWAY	7	BURLINGTON-GRAHAM MPO	I-6009	STATEWIDE MOBILITY	WILL BE REPRIORITIZED	T		\$700,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$100,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY
ALAMANCE	I-40 / I-85	SR 1981 (TROLLINGWOOD-HAWFIELDS ROAD) IN MEBANE. UPGRADE INTERCHANGE.	HIGHWAY	7	BURLINGTON-GRAHAM MPO	I-6059	DIVISION 7	WILL BE REPRIORITIZED	NHP		\$600,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$200,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY
ALAMANCE	NC 119	SR 1981 (TROLLINGWOOD-HAWFIELDS ROAD) / SR 2126 (OLD HILLSBOROUGH ROAD TO LOWES BOULEVARD IN MEBANE. WIDEN TO MULTILANES.	HIGHWAY	7	BURLINGTON-GRAHAM MPO	U-6013	DIVISION 7	SCHEDULED FOR DELIVERY	T	2023	\$4,228,000	2023	\$900,000	2024
ALAMANCE	NC 49 (ROXBORO ROAD)	SR 1928 (WILKINS ROAD) AND SR 1927 (BASON ROAD). UPGRADE K-TYPE INTERSECTION.	HIGHWAY	7	BURLINGTON-GRAHAM MPO	U-6183	DIVISION 7	WILL BE REPRIORITIZED	T		\$400,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$1,200,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY
ALAMANCE	NC 54 (CHAPEL HILL ROAD)	SR 1445 (SOUTH O'NEAL STREET) IN BURLINGTON. RECONFIGURE INTERSECTION TO MAKE O'NEAL STREET THE THROUGH MOVEMENT WITH NC 54 EAST OF THE INTERSECTION.	HIGHWAY	7	BURLINGTON-GRAHAM MPO	U-6184	DIVISION 7	WILL BE REPRIORITIZED	T		\$5,800,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$400,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY
ALAMANCE	NC 54 (EAST HARDEN STREET)	I-40 / I-85 INTERCHANGE IN GRAHAM. UPGRADE RAMP INTERSECTIONS.	HIGHWAY	7	BURLINGTON-GRAHAM MPO	U-6115B	REGION D	WILL BE REPRIORITIZED	T		\$600,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY	\$300,000	FUNDED FOR PRELIMINARY ENGINEERING ONLY

Next Steps / Schedule

2024-2033 STIP Next Steps / Schedule

Local Officials Education Webinar on May 17th

- Commissioners, Councilmembers, Mayors, Managers, etc.

STIP coordination meetings with MPO/RPOs as needed

Project swaps due to STIP managers by September 30th

Revised Draft STIP by December 2022

Public Involvement

Final 2024-2033 STIP to be adopted by BOT in Summer 2023

Prioritization Next Steps and Schedule

P7 Workgroup will likely begin Fall 2022

P7 should generate the 2026-2035 STIP

- Return to two-year Prioritization/STIP cycle

Anticipated P7 submittal window: Summer 2023


Anticipated P7 quantitative scores and 2026-2035 Statewide Mobility programming:
Spring 2024

2024-2033 STIP Next Steps / Schedule

PROGRAMMING



PRIORITIZATION 7.0

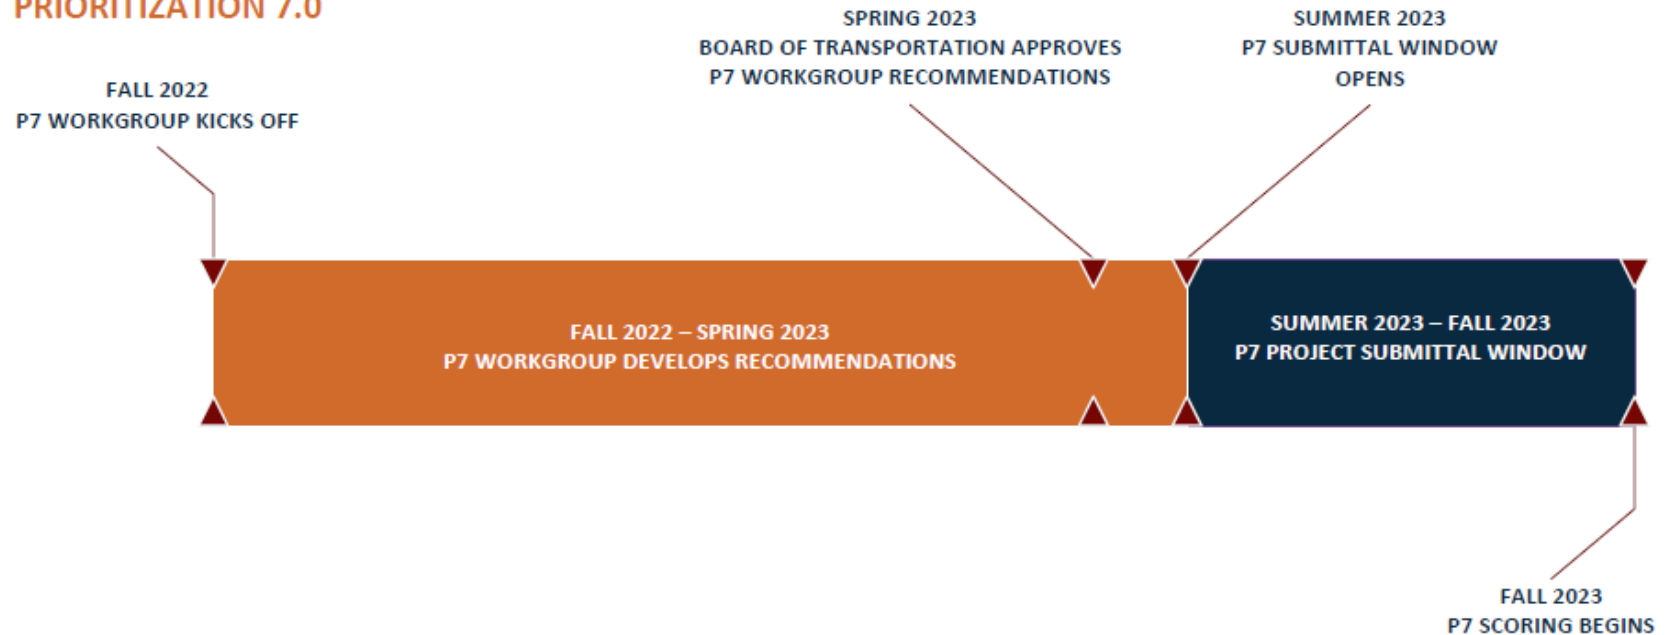

Discussion
